

UNCLASSIFIED



## Selected Acquisition Report (SAR)

RCS: DD-A&T(Q&A)823-101



### **H-1 Upgrades (4BW/4BN) (H-1 Upgrades)**

As of FY 2020 President's Budget

Defense Acquisition Management  
Information Retrieval  
(DAMIR)

---

UNCLASSIFIED

## Table of Contents

Sensitivity Originator .....	3
Common Acronyms and Abbreviations for MDAP Programs .....	4
Program Information .....	6
Responsible Office .....	6
References .....	7
Mission and Description .....	8
Executive Summary .....	9
Threshold Breaches .....	12
Schedule .....	13
Performance .....	15
Track to Budget .....	20
Cost and Funding .....	20
Low Rate Initial Production .....	30
Foreign Military Sales .....	31
Nuclear Costs .....	31
Unit Cost .....	32
Cost Variance .....	35
Contracts .....	38
Deliveries and Expenditures .....	43
Operating and Support Cost .....	44

**Sensitivity Originator**

No originator information is available at this time.

## Common Acronyms and Abbreviations for MDAP Programs

Acq O&M - Acquisition-Related Operations and Maintenance  
ACAT - Acquisition Category  
ADM - Acquisition Decision Memorandum  
APB - Acquisition Program Baseline  
APPN - Appropriation  
APUC - Average Procurement Unit Cost  
\$B - Billions of Dollars  
BA - Budget Authority/Budget Activity  
Blk - Block  
BY - Base Year  
CAPE - Cost Assessment and Program Evaluation  
CARD - Cost Analysis Requirements Description  
CDD - Capability Development Document  
CLIN - Contract Line Item Number  
CPD - Capability Production Document  
CY - Calendar Year  
DAB - Defense Acquisition Board  
DAE - Defense Acquisition Executive  
DAMIR - Defense Acquisition Management Information Retrieval  
DoD - Department of Defense  
DSN - Defense Switched Network  
EMD - Engineering and Manufacturing Development  
EVM - Earned Value Management  
FOC - Full Operational Capability  
FMS - Foreign Military Sales  
FRP - Full Rate Production  
FY - Fiscal Year  
FYDP - Future Years Defense Program  
ICE - Independent Cost Estimate  
IOC - Initial Operational Capability  
Inc - Increment  
JROC - Joint Requirements Oversight Council  
\$K - Thousands of Dollars  
KPP - Key Performance Parameter  
LRIP - Low Rate Initial Production  
\$M - Millions of Dollars  
MDA - Milestone Decision Authority  
MDAP - Major Defense Acquisition Program  
MILCON - Military Construction  
N/A - Not Applicable  
O&M - Operations and Maintenance  
ORD - Operational Requirements Document  
OSD - Office of the Secretary of Defense  
O&S - Operating and Support  
PAUC - Program Acquisition Unit Cost

PB - President's Budget  
PE - Program Element  
PEO - Program Executive Officer  
PM - Program Manager  
POE - Program Office Estimate  
RDT&E - Research, Development, Test, and Evaluation  
SAR - Selected Acquisition Report  
SCP - Service Cost Position  
TBD - To Be Determined  
TY - Then Year  
UCR - Unit Cost Reporting  
U.S. - United States  
USD(AT&L) - Under Secretary of Defense (Acquisition, Technology and Logistics)  
USD(A&S) - Under Secretary of Defense (Acquisition and Sustainment)

## Program Information

**Program Name**

H-1 Upgrades (4BW/4BN) (H-1 Upgrades)

**DoD Component**

Navy

## Responsible Office

Col David Walsh  
PMA-276 USMC Light/Attack Helicopter  
Program Executive Officer - Air, Anti-Submarine Warfare,  
Assault & Special Mission  
48202 Bronson Road, 2nd Floor  
Patuxent River, MD 20670-1547

**Phone:** 301-757-5534**Fax:** 301-342-3788**DSN Phone:** 757-5534**DSN Fax:** 342-3788**Date Assigned:** March 3, 2017[david.walsh@navy.mil](mailto:david.walsh@navy.mil)

## References

**SAR Baseline (Production Estimate)**

Defense Acquisition Executive (DAE) Approved Acquisition Program Baseline (APB) dated December 22, 2008

**Approved APB**

Navy Acquisition Executive (NAE) Approved Acquisition Program Baseline (APB) dated February 11, 2011

## Mission and Description

The AH-1Z and UH-1Y were designed as upgrades to the AH-1W and UH-1N aircraft. The mission of the AH-1Z attack helicopter is to provide rotary wing close air support, anti-armor, armed escort, armed/visual reconnaissance and fire support coordination capabilities under day/night and adverse weather conditions. The mission of the UH-1Y utility helicopter is to provide command, control and assault support under day/night and adverse weather conditions. Major modifications incorporated in the UH-1Y and AH-1Z include a new four-bladed rotor system and fully integrated common cockpits/avionics.



## Executive Summary

### Program Highlights Since Last Report

Production of H-1 aircraft continues at Bell Helicopter with final assembly and delivery occurring in Amarillo, Texas. There are 373 aircraft (Lots 1-16) on contract, which includes 10 UH-1Y remanufactured and 150 Build New UH-1Y, 37 AH-1Z remanufactured and 176 AH-1Z Build New (ZBN) aircraft (including 12 Pakistan and 12 Bahrain AH-1ZBN aircraft). As of March 18, 2019, 269 domestic production aircraft (160 UH-1Ys, 37 remanufactured AH-1Zs, and 72 AH-1ZBNs) have been delivered to the Fleet either on or ahead of schedule. The last UH-1Y production aircraft was delivered on April 30, 2018. The US Marine Corps program of record remains 349 aircraft (160 UH-1Ys and 189 AH-1Zs) and is fully funded.

The program office continues to execute Pakistan case PK-P-SBO (12 AH-1Zs) and completed delivery of the last aircraft on September 30, 2018. On October 7, 2018 Bahrain signed a Letter of Acceptance (LOA) to purchase 12 AH-1Zs with deliveries expected to start in CY 2021.

The program office continues to make progress on improving material availability and reliability while expanding depot capability. Readiness corrective action plans continue to progress and several improvements are being validated or have fielded, improving readiness over the past 12 months. Additional efforts are being pursued to continue to accelerate readiness recovery. Depot capability continues to increase across the Fleet Readiness Centers.

There are no significant software-related issues with this program at this time.

History of Significant Developments Since Program Initiation	
History of Significant Developments Since Program Initiation	
Date	Significant Development Description
September 1996	EMD Contract Award with Bell Helicopter
October 1996	Milestone II Decision received with the purpose of addressing deficiencies in operational capability, performance, power availability, reliability, availability, and maintainability of the legacy AH-1W and UH-1N aircraft
October 1996	Original APB Development
June 1997	Preliminary Design Review (PDR) Complete
September 1998	Critical Design Review (CDR) Complete
June 2000	APB Change #1 – Unfunded/underfunded program requirements identified; Increased overhead charges; Higher than planned labor rates; Subcontractor cost overruns
May 2002	Nunn McCurdy Breach – Cost increase due to underestimation of scope, program delays, requirements changes
May 2002	APB Change #2 – Revised business base assumptions; Increased rates due to reduction in V-22 quantities; Late design changes; Parts shortages; Added scope; Earned Value Management compliance issues
December 2003	Lot 1 Production contract award to Bell Helicopter procuring 6 UH-1Y, 3 AH-1Z Remanufactured
April 2005	Lot 2 Production contract award to Bell Helicopter procuring 4 UH-1Y, 3 AH-1Z Remanufactured
April 2005	APB Change #3 – Increased cost due to underestimation of scope, program delays, requirements changes
July 2006	Lot 3 Production contract award to Bell Helicopter procuring 7 UH-1Y
January 2007	Operational Evaluation (OPEVAL) Phase I Testing for UH-1Y and AH-1Z
July 2007	Lot 4 Production contract award to Bell Helicopter procuring 9 UH-1Y, 2 AH-1Z Remanufactured
July 2007	APB Change #4 – Cost estimates higher than budgeted; Increased rates and material costs; Delayed deliveries; Engineering and Suitability issues; System maturity delayed OPEVAL
January 2008	Lot 5 Production contract award to Bell Helicopter procuring 11 UH-1Y , 4 AH-1Z Remanufactured
April 2008	UH-1Y Initial Operational Test and Evaluation (IOT&E)
May 2008	OPEVAL Phase II Testing completed for UH-1Y
August 2008	UH-1Y achieved IOC
September 2008	UH-1Y approved for MS III/FRP
November 2008	Nunn McCurdy Breach – Increased Prime Contractor material/labor costs; Government Furnished Equipment (GFE); Non-recurring production investments; Operational Evaluation Phase I corrections; Increased procurement objective (280 to 349 Program of Record (POR) – Remanufactured versus AH-1Z Build New)
December 2008	Production APB – Revised OPEVAL Phase II update; Additional LRIPs added; Added separate MS III for AH-1Z; Various KPPs updated; Production Cost update; Program of Record quantity increase
March 2009	Lot 6 Production contract award to Bell Helicopter procuring 15 UH-1Y and 5 AH-1Z Remanufactured aircraft
February 2010	Lot 8 Production contract award to Bell Helicopter procuring 19 UH-1Y , 8 AH-1Z Remanufactured and 6 AH-1ZBNs



June 2010	Lot 7 Production contract award to Bell Helicopter procuring 18 UH-1Y , 9 AH-1Z Remanufactured and 2 AH-1ZBNs
July 2010	OPEVAL Phase II Testing AH-1Z
July 2010	AH-1Z IOT&E
November 2010	AH-1Z MS III/FRP
February 2011	AH-1Z achieved IOC
February 2011	Production APB Change #1 – Navy Support Date (NSD); Force Protection (seating) KPP update; Production Cost update
October 2012	Lot 9 Production contract award to Bell Helicopter procuring 15 UH-1Y , 3 AH-1Z Remanufactured and 7 AH-1ZBNs
December 2012	Lot 10 Production contract award to Bell Helicopter procuring 16 UH-1Y and 12 AH-1ZBNs
May 2013	Lot 11 Production contract award to Bell Helicopter procuring 12 UH-1Y and 12 AH-1ZBNs
March 2014	Lot 12 Production contract award to Bell Helicopter procuring 15 UH-1Y and 16 AH-1ZBNs
November 2014	Lot 13 Production contract award to Bell Helicopter procuring 27 AH-1ZBNs
February 2017	Lot 14 Production contract award to Bell Helicopter procuring 27 AH-1ZBNs
April 2018	Last UH-1Y aircraft delivered
August 2018	Lot 15 Production contract award to Bell Helicopter procuring 29 AH-1ZBNs
January 2019	Lot 16 Production contract award to Bell Helicopter procuring 25 AH-1ZBNs. Last domestic Lot Production Contract to satisfy POR of 349 aircraft.

## Threshold Breaches

### APB Breaches

<b>Schedule</b>		<input type="checkbox"/>
<b>Performance</b>		<input type="checkbox"/>
<b>Cost</b>	RDT&E	<input type="checkbox"/>
	Procurement	<input type="checkbox"/>
	MILCON	<input type="checkbox"/>
	Acq O&M	<input type="checkbox"/>
<b>O&amp;S Cost</b>		<input type="checkbox"/>
<b>Unit Cost</b>	PAUC	<input type="checkbox"/>
	APUC	<input type="checkbox"/>

### Nunn-McCurdy Breaches


#### Current UCR Baseline

PAUC	None
APUC	None

#### Original UCR Baseline

PAUC	None
APUC	None

### Schedule

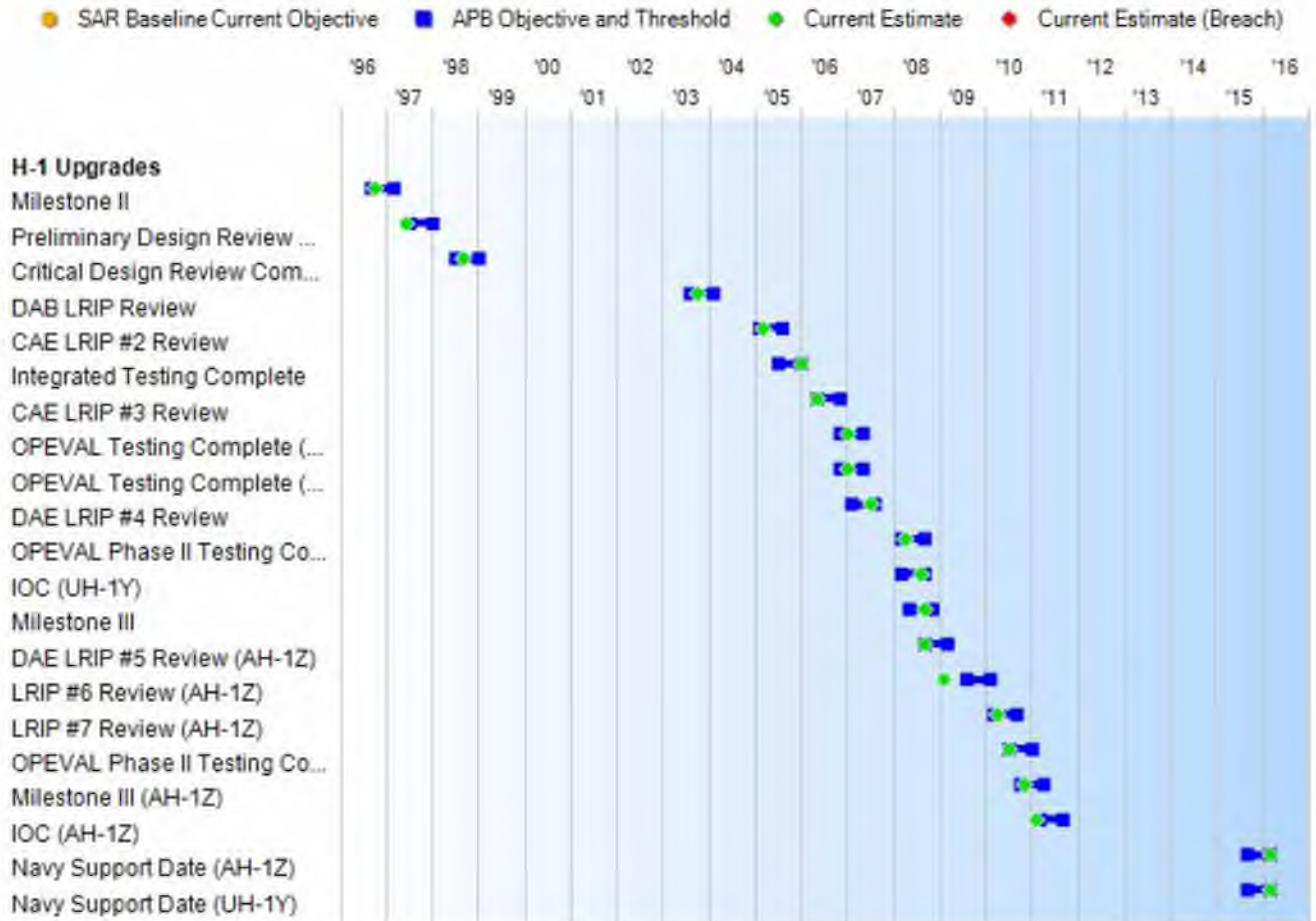

Schedule Events				
Events	SAR Baseline Production Estimate	Current APB Production Objective/Threshold		Current Estimate
Milestone II	Sep 1996	Sep 1996	Mar 1997	Oct 1996
Preliminary Design Review Complete	Jul 1997	Jul 1997	Jan 1998	Jun 1997
Critical Design Review Complete	Jul 1998	Jul 1998	Jan 1999	Sep 1998
DAB LRIP Review	Aug 2003	Aug 2003	Feb 2004	Oct 2003
CAE LRIP #2 Review	Feb 2005	Feb 2005	Aug 2005	Mar 2005
Integrated Testing Complete	Jul 2005	Jul 2005	Jan 2006	Jan 2006
CAE LRIP #3 Review	May 2006	May 2006	Nov 2006	May 2006
OPEVAL Testing Complete (AH-1Z)	Nov 2006	Nov 2006	May 2007	Jan 2007
OPEVAL Testing Complete (UH-1Y)	Nov 2006	Nov 2006	May 2007	Jan 2007
DAE LRIP #4 Review	Feb 2007	Feb 2007	Aug 2007	Jul 2007
OPEVAL Phase II Testing Complete (UH-1Y)	Mar 2008	Mar 2008	Sep 2008	Apr 2008
IOC (UH-1Y)	Mar 2008	Mar 2008	Sep 2008	Aug 2008
Milestone III	May 2008	May 2008	Nov 2008	Sep 2008
DAE LRIP #5 Review (AH-1Z)	Sep 2008	Sep 2008	Mar 2009	Sep 2008
LRIP #6 Review (AH-1Z)	Aug 2009	Aug 2009	Feb 2010	Feb 2009
LRIP #7 Review (AH-1Z)	Mar 2010	Mar 2010	Sep 2010	Apr 2010
OPEVAL Phase II Testing Complete (AH-1Z)	Jul 2010	Jul 2010	Jan 2011	Jul 2010
Milestone III (AH-1Z)	Oct 2010	Oct 2010	Apr 2011	Nov 2010
IOC (AH-1Z)	Mar 2011	Mar 2011	Sep 2011	Feb 2011
Navy Support Date (AH-1Z)	Mar 2012	Sep 2015	Mar 2016	Mar 2016
Navy Support Date (UH-1Y)	Mar 2012	Sep 2015	Mar 2016	Mar 2016

### Change Explanations

None

### Acronyms and Abbreviations

CAE - Component Acquisition Executive  
 OPEVAL - Operational Evaluation



## Performance

Performance Characteristics				
SAR Baseline Production Estimate	Current APB Production Objective/Threshold	Demonstrated Performance	Current Estimate	
<b>4BW (AH-1W/AH-1Z)</b>				
<b>MFHBA (hrs)</b>				
35.0	35.0	24.0	63.8	63.8
<b>MMH/FH (hrs)</b>				
3.6	3.6	4.3	2.5	2.5
<b>Cruise Speed (kts)</b>				
165	165	135	139	139
<b>Payload (Hot Day) (lbs)</b>				
3500 lbs	3500 lbs	2500 lbs 6 Wing Stations 4 Universal Under Wing Stations	3429	3429
<b>Weapon Stations</b>				
<b>Universal Mounts</b>				
6	6	4	4	4
<b>Precision Guided Munitions</b>				
16	16	12	16	16
<b>Maneuverability/Agility (G's)</b>				
-0.5 to +2.5	-0.5 to +2.5	-0.5 to +2.5	-0.5 to +2.5	-0.5 to +2.5
<b>Mission Radius (NM)</b>				
200 NM	200 NM	110 NM	135 NM x 1	135 NM x 1
<b>Shipboard Compatibility</b>				
Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.
<b>Interoperability</b>				
The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net Centric military	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military	The system must fully support execution of joint critical operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for transition to Net-	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net Centric military	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net Centric military



operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	operations to include: 1) DISR-mandated GIG IT standards and profiles identified in the TV-1, 2) DISR-mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	Centric military operations to include: 1) DISR-mandated GIG IT standards and profiles identified in the TV-1, 2) DISR-mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an IATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.
---	---	---	---	---

**Force Protection (Seating)**

Two AH-1Z pilot seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two AH-1Z pilot seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two AH-1Z pilot seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two AH-1Z pilot seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10Gs laterally.	Two AH-1Z pilot seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10Gs laterally.
--	--	--	---	---

**Survivability (Ballistic Tolerance/Hardening)**

Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 23 mm HEI.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 23 mm HEI.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.
--	--	--	--	--

**4BN (UH-1N/UH-1Y)****MFHBA (hrs)**



40.2	40.2	33.1	56.6	56.6
<b>MMH/FH (hrs)</b>				
2.9	2.9	3.9	2.0	2.0
<b>Cruise Speed (kts)</b>				
165	165	140	155	155
<b>Payload (Hot Day) (lbs)</b>				
4500	4500	2800	2982	2982
<b>Weapon Stations</b>				
2 Univ. Mounts	2 Univ. Mounts	2 Hard Mounts	2 Hard Mounts	2 Hard Mounts
<b>Maneuverability/Agility (G's)</b>				
-0.5 to +2.5	-0.5 to +2.5	-0.5 to +2.3	-0.5 to +2.3	-0.5 to +2.3
<b>Mission Radius (NM)</b>				
200 NM	200 NM	110 NM	130 NM	130 NM
<b>Shipboard Compatibility</b>				
Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.	Fully compatible to include blade fold.
<b>Interoperability</b>				
The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and non-repudiation,	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military operations to include: 1) DISR-mandated GIG IT standards and profiles identified in the TV-1, 2) DISR-mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and	The system must fully support execution of joint critical operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for transition to Net-Centric military operations to include: 1) DISR-mandated GIG IT standards and profiles identified in the TV-1, 2) DISR-mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication,	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and	The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military operations to include: 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration table, 3) NCOW RM Enterprise Services 4) Information assurance requirements including availability, integrity, authentication, confidentiality, and



and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	confidentiality, and non-repudiation, and issuance of an IATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.	non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture views.
---	--	--	--	--

#### Force Protection (Seating)

Two UH-1Y pilot seats and ten UH-1Y cabin seats that are stroking, crash-worthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two UH-1Y pilot seats and ten UH-1Y cabin seats that are stroking, crash-worthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two UH-1Y pilot seats and ten UH-1Y cabin seats that are stroking, crash-worthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10 Gs laterally.	Two UH-1Y pilot seats and ten UH-1Y cabin seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10Gs laterally.	Two UH-1Y pilot seats and ten UH-1Y cabin seats that are stroking, crashworthy, and capable of sustaining 20Gs longitudinal, 20Gs vertical, and 10Gs laterally.
---	---	---	---	---

#### Survivability (Ballistic Tolerance/Hardening)

Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 23 mm HEI.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 23 mm HEI.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.	Airframe structure and flight critical systems shall be ballistic tolerant/hardened against 12.7 mm API.
--	--	--	--	--

#### Requirements Reference

UH-1Y CPD and AH-1Z CPD dated June 11, 2007 as modified by JROC Memorandum 195-08 dated October 14, 2008

#### Change Explanations

None

**Acronyms and Abbreviations**

API - Armor Piercing Incendiary  
ATO - Authority to Operate  
DAA - Designated Approving Authority  
DISR - DoD Information Technology Standards Registry  
FRACAS - Failure Reporting, Analysis and Corrective Action System  
G's - Gravitational forces  
GIG - Global Information Grid  
HEI - High Explosive Incendiary  
hrs - Hours  
IATO - Interim Authority to Operate  
IT - Information Technology  
KIP - Key Interface Protocol  
kts - Knots  
lbs - Pounds  
MFHBA - Mean Flight Hours Between Abort  
mm - Millimeter  
MMH/FH - Maintenance Man Hours per Flight Hours  
NCOW - Net-Centric Operation and Warfare  
NM - Nautical Miles  
R&M - Reliability and Maintainability  
RM - Reference Model  
TV-1 - Technical Standards Profile  
Univ. - Universal

**Track to Budget****RDT&E**

Appn	BA	PE
------	----	----

Navy 1319 05 0604245N

Project	Name
---------	------

2279 H-1 Upgrades (Sunk)

**Procurement**

Appn	BA	PE
------	----	----

Navy 1506 01 0206131M

Line Item	Name
-----------	------

0178 H-1 Upgrades (UH-1Y/AH-1Z)

Navy 1506 06 0206131M

Line Item	Name
-----------	------

0605 Spares and Repair Parts (Sunk)

**MILCON**

Appn	BA	PE
------	----	----

Navy 1205 01 0216496M

Project	Name
---------	------

991 H-1 Y/Z Helicopter Gearbox Repair & Test Facility (Sunk)



## Cost and Funding

### Cost Summary

Total Acquisition Cost							
Appropriation	BY 2008 \$M			BY 2008 \$M	TY \$M		
	SAR Baseline Production Estimate	Current APB Production Objective/Threshold		Current Estimate	SAR Baseline Production Estimate	Current APB Production Objective	Current Estimate
RDT&E	1799.2	1848.3	2033.1	1704.0	1644.1	1696.2	1537.1
Procurement	9404.2	10088.4	11097.2	9922.2	10542.7	11022.1	10923.4
Flyaway	--	--	--	8335.7	--	--	9234.1
Recurring	--	--	--	7845.5	--	--	8720.5
Non Recurring	--	--	--	490.2	--	--	513.6
Support	--	--	--	1586.5	--	--	1689.3
Other Support	--	--	--	1340.8	--	--	1441.6
Initial Spares	--	--	--	245.7	--	--	247.7
MILCON	0.0	16.3	17.9	16.0	0.0	17.6	17.6
Acq O&M	0.0	0.0	--	0.0	0.0	0.0	0.0
Total	11203.4	11953.0	N/A	11642.2	12186.8	12735.9	12478.1

#### Cost Notes

No cost estimate for the program has been completed in the previous year.

H-1 airframe contract savings of \$158M (FY 2018/2019 APN-1) identified as a source for the CH-53K Above Threshold Reprogramming (ATR) request submitted to Congress. Funding remains included in this estimate given the ATR request is pending Congressional approval.

Total Quantity			
Quantity	SAR Baseline Production Estimate	Current APB Production	Current Estimate
RDT&E		4	4
Procurement		349	349
Total		353	353

#### Quantity Notes

The four RDT&E aircraft include two UH-1Ys and two AH-1Zs. The 349 Procurement aircraft include 37 AH-1W helicopters remanufactured into AH-1Zs, 152 AH-1Z Build New models, 10 UH-1N helicopters remanufactured into UH-1Ys, and 150 new UH-1Y models. Program currently funded to Program of Record 349 aircraft.

**Cost and Funding****Funding Summary**

Appropriation Summary									
FY 2020 President's Budget / December 2018 SAR (TY\$ M)									
Appropriation	Prior	FY 2019	FY 2020	FY 2021	FY 2022	FY 2023	FY 2024	To Complete	Total
RDT&E	1537.1	0.0	0.0	0.0	0.0	0.0	0.0	0.0	1537.1
Procurement	10032.6	798.4	62.0	7.4	7.5	7.7	7.8	0.0	10923.4
MILCON	17.6	0.0	0.0	0.0	0.0	0.0	0.0	0.0	17.6
Acq O&M	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
PB 2020 Total	11587.3	798.4	62.0	7.4	7.5	7.7	7.8	0.0	12478.1
PB 2019 Total	11375.9	820.8	62.7	7.7	7.8	8.0	2.0	0.0	12284.9
Delta	211.4	-22.4	-0.7	-0.3	-0.3	-0.3	5.8	0.0	193.2

Quantity Summary										
FY 2020 President's Budget / December 2018 SAR (TY\$ M)										
Quantity	Undistributed	Prior	FY 2019	FY 2020	FY 2021	FY 2022	FY 2023	FY 2024	To Complete	Total
Development	4	0	0	0	0	0	0	0	0	4
Production	0	324	25	0	0	0	0	0	0	349
PB 2020 Total	4	324	25	0	0	0	0	0	0	353
PB 2019 Total	4	317	25	0	0	0	0	0	0	346
Delta	0	7	0	0	0	0	0	0	0	7

## Cost and Funding

### Annual Funding By Appropriation

Annual Funding							
1319   RDT&E   Research, Development, Test, and Evaluation, Navy							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1996	--	--	--	--	--	--	10.9
1997	--	--	--	--	--	--	67.9
1998	--	--	--	--	--	--	81.3
1999	--	--	--	--	--	--	116.7
2000	--	--	--	--	--	--	178.5
2001	--	--	--	--	--	--	138.2
2002	--	--	--	--	--	--	167.4
2003	--	--	--	--	--	--	232.9
2004	--	--	--	--	--	--	99.1
2005	--	--	--	--	--	--	168.2
2006	--	--	--	--	--	--	58.6
2007	--	--	--	--	--	--	26.4
2008	--	--	--	--	--	--	12.6
2009	--	--	--	--	--	--	4.4
2010	--	--	--	--	--	--	28.1
2011	--	--	--	--	--	--	57.6
2012	--	--	--	--	--	--	60.6
2013	--	--	--	--	--	--	27.7
Subtotal	4	--	--	--	--	--	1537.1



Annual Funding							
1319   RDT&E   Research, Development, Test, and Evaluation, Navy							
Fiscal Year	Quantity	BY 2008 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1996	--	--	--	--	--	--	13.3
1997	--	--	--	--	--	--	82.0
1998	--	--	--	--	--	--	97.4
1999	--	--	--	--	--	--	138.1
2000	--	--	--	--	--	--	208.3
2001	--	--	--	--	--	--	159.1
2002	--	--	--	--	--	--	190.7
2003	--	--	--	--	--	--	261.5
2004	--	--	--	--	--	--	108.3
2005	--	--	--	--	--	--	179.0
2006	--	--	--	--	--	--	60.5
2007	--	--	--	--	--	--	26.6
2008	--	--	--	--	--	--	12.5
2009	--	--	--	--	--	--	4.3
2010	--	--	--	--	--	--	27.0
2011	--	--	--	--	--	--	54.1
2012	--	--	--	--	--	--	56.0
2013	--	--	--	--	--	--	25.3
Subtotal	4	--	--	--	--	--	1704.0



Annual Funding								
1506   Procurement   Aircraft Procurement, Navy								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	--	--	--	--	--	6.0	6.0	
2002	--	--	--	--	--	--	--	
2003	--	--	--	--	--	--	--	
2004	9	197.8	--	23.8	221.6	105.9	327.5	
2005	7	136.9	--	18.7	155.6	78.3	233.9	
2006	7	150.9	--	42.2	193.1	162.0	355.1	
2007	11	228.8	--	136.5	365.3	170.1	535.4	
2008	15	315.5	--	25.2	340.7	154.3	495.0	
2009	24	514.0	--	42.6	556.6	80.5	637.1	
2010	27	655.7	--	34.8	690.5	70.7	761.2	
2011	31	688.5	--	77.6	766.1	127.0	893.1	
2012	25	567.6	--	46.3	613.9	120.0	733.9	
2013	30	772.8	--	3.8	776.6	89.6	866.2	
2014	23	574.3	--	1.6	575.9	85.6	661.5	
2015	31	792.3	--	--	792.3	106.8	899.1	
2016	29	780.5	--	--	780.5	60.3	840.8	
2017	26	759.8	--	6.4	766.2	88.8	855.0	
2018	29	864.5	--	--	864.5	67.3	931.8	
2019	25	720.6	--	--	720.6	77.8	798.4	
2020	--	--	--	54.1	54.1	7.9	62.0	
2021	--	--	--	--	--	7.4	7.4	
2022	--	--	--	--	--	7.5	7.5	
2023	--	--	--	--	--	7.7	7.7	
2024	--	--	--	--	--	7.8	7.8	
Subtotal	349	8720.5	--	513.6	9234.1	1689.3	10923.4	

Annual Funding								
1506   Procurement   Aircraft Procurement, Navy								
Fiscal Year	Quantity	BY 2008 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	--	--	--	--	--	--	6.8	6.8
2002	--	--	--	--	--	--	--	--
2003	--	--	--	--	--	--	--	--
2004	9	212.6	--	25.6	238.2	113.8	352.0	352.0
2005	7	143.1	--	19.6	162.7	81.8	244.5	244.5
2006	7	153.5	--	42.9	196.4	164.8	361.2	361.2
2007	11	227.5	--	135.7	363.2	169.1	532.3	532.3
2008	15	309.0	--	24.7	333.7	151.1	484.8	484.8
2009	24	496.5	--	41.2	537.7	77.7	615.4	615.4
2010	27	620.4	--	32.9	653.3	66.9	720.2	720.2
2011	31	638.8	--	72.0	710.8	117.8	828.6	828.6
2012	25	519.1	--	42.3	561.4	109.8	671.2	671.2
2013	30	699.2	--	3.4	702.6	81.2	783.8	783.8
2014	23	512.9	--	1.4	514.3	76.5	590.8	590.8
2015	31	697.1	--	--	697.1	94.0	791.1	791.1
2016	29	672.8	--	--	672.8	52.0	724.8	724.8
2017	26	642.0	--	5.4	647.4	75.0	722.4	722.4
2018	29	715.9	--	--	715.9	55.8	771.7	771.7
2019	25	585.1	--	--	585.1	63.1	648.2	648.2
2020	--	--	--	43.1	43.1	6.3	49.4	49.4
2021	--	--	--	--	--	5.8	5.8	5.8
2022	--	--	--	--	--	5.7	5.7	5.7
2023	--	--	--	--	--	5.8	5.8	5.8
2024	--	--	--	--	--	5.7	5.7	5.7
Subtotal	349	7845.5	--	490.2	8335.7	1586.5	9922.2	9922.2

Cost Quantity Information		
1506   Procurement   Aircraft Procurement, Navy		
Fiscal Year	Quantity	End Item Recurring Flyaway (Aligned With Quantity) BY 2008 \$M
2001	--	--
2002	--	--
2003	--	--
2004	9	212.6
2005	7	143.1
2006	7	153.5
2007	11	227.5
2008	15	309.0
2009	24	496.5
2010	27	572.7
2011	31	632.4
2012	25	521.2
2013	30	693.0
2014	23	517.6
2015	31	694.9
2016	29	680.2
2017	26	648.8
2018	29	722.6
2019	25	619.9
2020	--	--
2021	--	--
2022	--	--
2023	--	--
2024	--	--
Subtotal	349	7845.5

Annual Funding 1205   MILCON   Military Construction, Navy and Marine Corps	
Fiscal Year	TY \$M
	Total Program
2012	17.6
Subtotal	17.6

Annual Funding 1205   MILCON   Military Construction, Navy and Marine Corps	
Fiscal Year	BY 2008 \$M
	Total Program
2012	16.0
Subtotal	16.0



## Low Rate Initial Production

Item	Initial LRIP Decision	Current Total LRIP
<b>Approval Date</b>	10/22/2003	6/7/2010
<b>Approved Quantity</b>	28	55
<b>Reference</b>	LRIP ADM	LRIP VII ADM
<b>Start Year</b>	2004	2004
<b>End Year</b>	2005	2010

The Current Total LRIP Quantity is more than 10% of the total production quantity due to the need to permit an orderly increase in the production rate and efficiency until successful completion of operational testing.

## Foreign Military Sales

Country	Date of Sale	Quantity	Total Cost \$M	Description
Bahrain	11/28/2018	12	658.5	FMS Case BA-P-BSO, AH-1Z helicopters, initial support, and training.
Pakistan	7/10/2015	12	621.4	FMS Case PK-P-BSO, AH-1Z helicopters, initial support, and training.

### Notes

Total Cost reflects the total Case value as defined by the signed and implemented Letter of Offer and Acceptance (LOA) for both Pakistan and Bahrain.


## Nuclear Costs

None

**Unit Cost**

Current UCR Baseline and Current Estimate (Base-Year Dollars)			
Item	BY 2008 \$M	BY 2008 \$M	% Change
	Current UCR Baseline (Feb 2011 APB)	Current Estimate (Dec 2018 SAR)	
Program Acquisition Unit Cost			
Cost	11953.0	11642.2	
Quantity	353	353	
Unit Cost	33.861	32.981	-2.60
Average Procurement Unit Cost			
Cost	10088.4	9922.2	
Quantity	349	349	
Unit Cost	28.907	28.430	-1.65
Original UCR Baseline and Current Estimate (Base-Year Dollars)			
Item	BY 2008 \$M	BY 2008 \$M	% Change
	Revised Original UCR Baseline (Apr 2005 APB)	Current Estimate (Dec 2018 SAR)	
Program Acquisition Unit Cost			
Cost	7852.2	11642.2	
Quantity	284	353	
Unit Cost	27.649	32.981	+19.28
Average Procurement Unit Cost			
Cost	6352.9	9922.2	
Quantity	280	349	
Unit Cost	22.689	28.430	+25.30



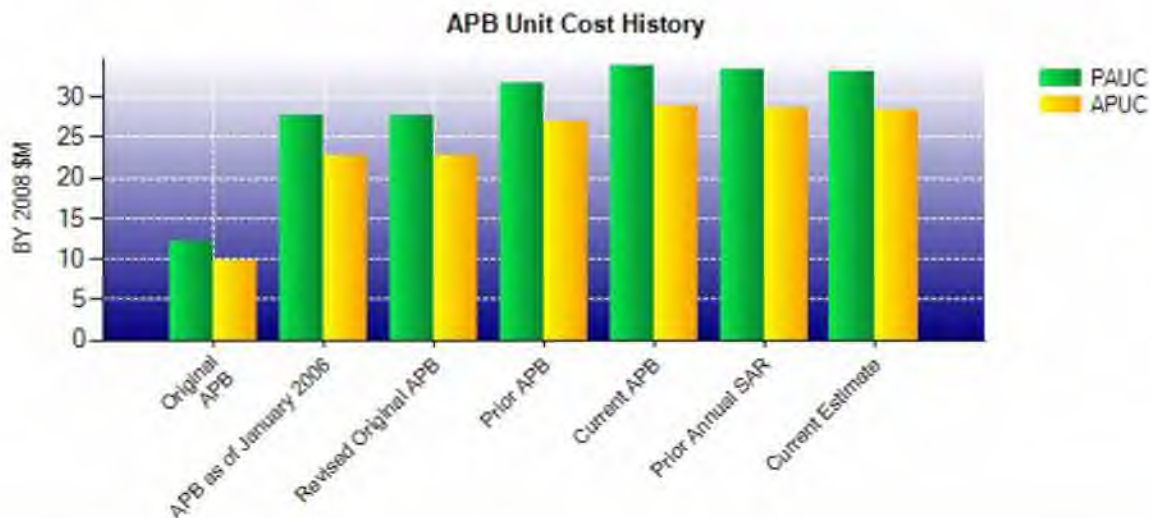

APB Unit Cost History					
Item	Date	BY 2008 \$M		TY \$M	
		PAUC	APUC	PAUC	APUC
Original APB	Oct 1996	12.089	9.903	12.491	10.554
APB as of January 2006	Apr 2005	27.649	22.689	28.172	23.843
Revised Original APB	Apr 2005	27.649	22.689	28.172	23.843
Prior APB	Dec 2008	31.738	26.946	34.524	30.208
Current APB	Feb 2011	33.861	28.907	36.079	31.582
Prior Annual SAR	Dec 2017	33.251	28.611	35.505	31.375
Current Estimate	Dec 2018	32.981	28.430	35.349	31.299

**SAR Unit Cost History**

Initial SAR Baseline to Current SAR Baseline (TY \$M)									
Initial PAUC Development Estimate	Changes								PAUC Production Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
12.491	-0.078	-1.056	1.772	2.351	15.397	0.000	3.647	22.033	34.524

Current SAR Baseline to Current Estimate (TY \$M)									
PAUC Production Estimate	Changes								PAUC Current Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
34.524	-0.654	-0.026	-0.073	0.274	1.286	0.000	0.018	0.825	35.349

Initial SAR Baseline to Current SAR Baseline (TY \$M)									
Initial APUC Development Estimate	Changes								APUC Production Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
10.554	-0.003	-0.686	1.722	1.632	13.299	0.000	3.690	19.654	30.208

Current SAR Baseline to Current Estimate (TY \$M)									
APUC Production Estimate	Changes								APUC Current Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
30.208	-0.670	-0.025	-0.074	0.000	1.841	0.000	0.019	1.091	31.299

SAR Baseline History				
Item	SAR Planning Estimate	SAR Development Estimate	SAR Production Estimate	Current Estimate
Milestone I	N/A	N/A	N/A	N/A
Milestone II	N/A	Sep 1996	Sep 1996	Oct 1996
Milestone III	N/A	Feb 2004	May 2008	Sep 2008
IOC	N/A	Jun 2005	Mar 2008	Aug 2008
Total Cost (TY \$M)	N/A	3547.5	12186.8	12478.1
Total Quantity	N/A	284	353	353
PAUC	N/A	12.491	34.524	35.349

**Cost Variance**

Summary TY \$M				
Item	RDT&E	Procurement	MILCON	Total
SAR Baseline (Production Estimate)	1644.1	10542.7	--	12186.8
Previous Changes				
Economic	+2.3	-260.6	+0.3	-258.0
Quantity	--	-197.1	--	-197.1
Schedule	--	-17.9	--	-17.9
Engineering	+96.7	--	--	+96.7
Estimating	-206.0	+665.8	+17.3	+477.1
Other	--	--	--	--
Support	--	-2.7	--	-2.7
Subtotal	-107.0	+187.5	+17.6	+98.1
Current Changes				
Economic	+0.1	+26.9	--	+27.0
Quantity	--	+188.2	--	+188.2
Schedule	--	-7.9	--	-7.9
Engineering	--	--	--	--
Estimating	-0.1	-23.2	--	-23.3
Other	--	--	--	--
Support	--	+9.2	--	+9.2
Subtotal	--	+193.2	--	+193.2
Total Changes	-107.0	+380.7	+17.6	+291.3
CE - Cost Variance	1537.1	10923.4	17.6	12478.1
CE - Cost & Funding	1537.1	10923.4	17.6	12478.1



Summary BY 2008 \$M				
Item	RDT&E	Procurement	MILCON	Total
SAR Baseline (Production Estimate)	1799.2	9404.2	--	11203.4
Previous Changes				
Economic	--	--	--	--
Quantity	--	-158.7	--	-158.7
Schedule	--	-24.1	--	-24.1
Engineering	+83.6	--	--	+83.6
Estimating	-178.7	+566.5	+16.0	+403.8
Other	--	--	--	--
Support	--	-3.0	--	-3.0
Subtotal	-95.1	+380.7	+16.0	+301.6
Current Changes				
Economic	--	--	--	--
Quantity	--	+153.1	--	+153.1
Schedule	--	-3.1	--	-3.1
Engineering	--	--	--	--
Estimating	-0.1	-19.8	--	-19.9
Other	--	--	--	--
Support	--	+7.1	--	+7.1
Subtotal	-0.1	+137.3	--	+137.2
Total Changes	-95.2	+518.0	+16.0	+438.8
CE - Cost Variance	1704.0	9922.2	16.0	11642.2
CE - Cost & Funding	1704.0	9922.2	16.0	11642.2

Previous Estimate: December 2017

RDT&E	\$M	
Current Change Explanations	Base Year	Then Year
Revised escalation indices. (Economic)	N/A	+0.1
Adjustment for current and prior escalation. (Estimating)	-0.1	-0.1
<b>RDT&amp;E Subtotal</b>	<b>-0.1</b>	<b>0.0</b>

Procurement	\$M	
Current Change Explanations	Base Year	Then Year
Revised escalation indices. (Economic)	N/A	+26.9
Adjustment for current and prior escalation. (Estimating)	-20.0	-23.5
Total Quantity variance resulting from an increase of seven helicopters from 342 to 349. (Subtotal)	+162.6	+200.3
Quantity variance resulting from an increase of seven helicopters from 342 to 349. (Quantity)	(+143.9)	(+177.2)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-0.5)	(-0.6)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(+19.2)	(+23.7)
Additional Quantity variance resulting from increase of seven helicopters. (Quantity)	+9.2	+11.0
Schedule variance resulting from rephasing seven additional helicopters from FY 2019 to FY 2018. (Schedule)	0.0	-3.9
Additional Schedule variance resulting from rephasing seven additional helicopters from FY 2019 to FY 2018. (Schedule)	-2.6	-3.4
Revised estimate for Airframe cost. (Estimating)	-18.2	-22.4
Revised estimate to reflect the application of new outyear inflation indices. (Estimating)	-0.8	-1.0
Adjustment for current and prior escalation. (Support)	-1.9	-2.6
Increase in Other Support due to updated support strategy. (Support)	+9.0	+11.8
<b>Procurement Subtotal</b>	<b>+137.3</b>	<b>+193.2</b>

(QR) Quantity Related



## Contracts

### Contract Identification

**Appropriation:** Procurement  
**Contract Name:** H-1 Upgrades Production Contract Lot 12  
**Contractor:** Bell Helicopter Textron Inc.  
**Contractor Location:** 600 E Hurst Blvd  
 Hurst, TX 76053  
**Contract Number:** N00019-13-C-0023/12  
**Contract Type:** Fixed Price Incentive(Firm Target) (FPIF)  
**Award Date:** March 27, 2014  
**Definitization Date:** August 25, 2015

### Contract Price

Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
59.7	59.7	26	648.3	661.0	34	648.3	648.3

### Target Price Change Explanation

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to the award of Advance Procurement of long lead items and contract definitization. Lot 12 includes three FMS Pakistan AH-1Z Build New aircraft. The contract also includes Firm Fixed Price and Cost Plus Fixed Fee Acquisition Logistics Support and Systems Engineering/Program Management efforts.

### Contract Variance

Item	Cost Variance	Schedule Variance
Cumulative Variances To Date (12/2/2017)	+27.2	-20.7
Previous Cumulative Variances	+27.2	-20.7
Net Change	+0.0	+0.0

### Cost and Schedule Variance Explanations

None

### General Contract Variance Explanation

Cost and schedule variances are no longer reported for this contract. The last aircraft was delivered in May 2018.

### Notes

This contract is more than 90% complete; therefore, this is the final report for this contract.

**Contract Identification**

**Appropriation:** Procurement  
**Contract Name:** H-1 Upgrades Production Contract Lot 13  
**Contractor:** Bell Helicopter Textron  
**Contractor Location:** 600 E. Hurst Blvd  
Hurst, TX 76053  
**Contract Number:** N00019-13-C-0023/13  
**Contract Type:** Fixed Price Incentive(Firm Target) (FPIF)  
**Award Date:** August 25, 2015  
**Definitization Date:** March 14, 2016

**Contract Price**

Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
58.1	58.1	29	742.2	756.0	38	742.2	742.2

**Target Price Change Explanation**

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to the award of Advance Procurement of long lead items and contract definitization. Lot 13 includes one FY 2014 funded aircraft and nine FMS Pakistan AH-1Z Build New aircraft. The contract also includes Firm Fixed Price and Cost Plus Fixed Fee Acquisition Logistics Support and Systems Engineering/Program Management (SEPM) efforts through CY2018.

**Contract Variance**

Item	Cost Variance	Schedule Variance
Cumulative Variances To Date (2/2/2019)	+48.8	-2.2
Previous Cumulative Variances	+16.0	-53.4
Net Change	+32.8	+51.2

**Cost and Schedule Variance Explanations**

The favorable net change in the cost variance is due to favorable manufacturing performance and material prices.

The favorable net change in the schedule variance is due to the recovery of late delivery of cabin parts and other material.

**Notes**

This contract is more than 90% complete; therefore, this is the final report for this contract.



**Contract Identification**

**Appropriation:** Procurement  
**Contract Name:** H-1 Upgrades Production Contract Lot 14  
**Contractor:** Bell Helicopter Textron  
**Contractor Location:** 600 E. Hurst Blvd  
 Hurst, TX 76053  
**Contract Number:** N00019-16-C-0003/14  
**Contract Type:** Fixed Price Incentive(Firm Target) (FPIF)  
**Award Date:** March 14, 2016  
**Definitization Date:** February 08, 2017

**Contract Price**

Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
55.9	55.9	25	517.7	527.9	27	517.7	517.7

**Target Price Change Explanation**

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to the award of Advance Procurement of long lead items and contract definitization. Lot 14 includes one FY 2016 funded aircraft. Increase is due to addition of two AH-1Z aircraft in November 2017.

**Contract Variance**

Item	Cost Variance	Schedule Variance
Cumulative Variances To Date (2/2/2019)	+2.9	-21.2
Previous Cumulative Variances	-0.1	+1.2
Net Change	+3.0	-22.4

**Cost and Schedule Variance Explanations**

The favorable net change in the cost variance is due to the contractor's restructure of their Material Requirements Planning.

The unfavorable net change in the schedule variance is due to various parts needed to support the production line were behind the baseline schedule.



**Contract Identification**

**Appropriation:** Procurement  
**Contract Name:** H-1 Upgrades Production Contract Lot 15  
**Contractor:** Bell Helicopter Textron, Inc.  
**Contractor Location:** 600 E Hurst Blvd  
Hurst, TX 76053  
**Contract Number:** N00019-17-C-0030/15  
**Contract Type:** Fixed Price Incentive(Firm Target) (FPIF)  
**Award Date:** February 07, 2017  
**Definitization Date:** August 23, 2018

**Contract Price**

Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
49.1	N/A	22	554.3	563.4	29	554.3	554.3

**Target Price Change Explanation**

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to the increase in target price is attributed to the definitization of Lot 15 to include 7 additional aircraft.

**Contract Variance**

Item	Cost Variance	Schedule Variance
Cumulative Variances To Date (2/2/2019)	+0.6	+6.6
Previous Cumulative Variances	--	--
Net Change	+0.6	+6.6

**Cost and Schedule Variance Explanations**

The favorable cumulative cost variance is due to early production efforts.

The favorable cumulative schedule variance is due to early production efforts.

**Contract Identification**

**Appropriation:** Procurement  
**Contract Name:** H-1 Upgrades Production Contract Lot 16  
**Contractor:** Bell Helicopter Textron  
**Contractor Location:** 600 E. Hurst Blvd  
 Hurst, TX 76053  
**Contract Number:** N00019-17-C-0030/16  
**Contract Type:** Fixed Price Incentive(Firm Target) (FPIF)  
**Award Date:** January 18, 2019  
**Definitization Date:**

**Contract Price**

Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
37.6	N/A	18	481.6	494.0	25	481.6	481.6

**Target Price Change Explanation**

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to the award of FY 2019 Advanced Procurement funds for Long Lead Items associated with the additional 7 aircraft.

**Cost and Schedule Variance Explanations**

Cost and Schedule Variance reporting is not required on this (FPIF) contract.

**General Contract Variance Explanation**

Cost and schedule variances are not reported for this contract because earned value management reporting has not yet commenced.

**Notes**

This is the first time this contract is being reported.

Lot 16 was awarded as an option under the Lot 15 contract.

## Deliveries and Expenditures

Deliveries				
Delivered to Date	Planned to Date	Actual to Date	Total Quantity	Percent Delivered
Development	4	4	4	100.00%
Production	269	269	349	77.08%
Total Program Quantity Delivered	273	273	353	77.34%

Expended and Appropriated (TY \$M)			
Total Acquisition Cost	12478.1	Years Appropriated	24
Expended to Date	10556.0	Percent Years Appropriated	82.76%
Percent Expended	84.60%	Appropriated to Date	12385.7
Total Funding Years	29	Percent Appropriated	99.26%

The above data is current as of March 11, 2019.

### Notes

Program of Record remains 349 aircraft.



## Operating and Support Cost

### Cost Estimate Details

<b>Date of Estimate:</b>	February 04, 2019
<b>Source of Estimate:</b>	POE
<b>Quantity to Sustain:</b>	349
<b>Unit of Measure:</b>	Aircraft
<b>Service Life per Unit:</b>	30.00 Years
<b>Fiscal Years in Service:</b>	FY 2007 - FY 2051

The program of record for H-1 Upgrades is 349 production aircraft. This quantity is reflected in the O&S cost estimate. The four development aircraft are EMD assets that are not assigned to the fleet and will not be sustained.

2019 inflation rates are included in this estimate.

PB 2019 Flight Hour controls are used in this estimate. H-1 Procurement Profile: 189 AH-1Z, 160 UH-1Y.

H-1 Primary Aircraft Authorization profile: 145 AH-1Z, 119 UH-1Y which does not include test assets. Combined squadrons are composed of 15 AH-1Z and 12 UH-1Y aircraft. The role of the 80 aircraft that are not part of the Primary Aircraft Authorization profile is to allow for scheduled and unscheduled depot level maintenance, modifications, inspections, and repairs without reduction of aircraft available for the assigned mission.

The life cycle includes a 30-year service life with an average annual usage of 296.4 flight hours per AH-1Z aircraft and an average annual usage of 224.4 flight hours per UH-1Y aircraft. The life cycle includes a total of 8,089 operating aircraft years derived from the Primary Authorized Aircraft from the latest Aircraft Program Data File and a manual squadron ramp down based on attrition and the estimated service life.

Each aircraft has a designed fatigue life of 10,000 hours per aircraft.

Average attrition rate is 0.9% for AH-1Z and UH-1Y.

Average pipeline rate is 7% for AH-1Z and UH-1Y.

Maintenance Costs consisting of Aviation Depot Level Repairable and Consumables are estimated using a bottoms-up model, utilizing historical costs and demand rates for both the UH-1Y and AH-1Z.

O&S cost estimate is based on three levels of organic maintenance with chargeable manning (fleet squadron) estimated at 100%.

### Sustainment Strategy

The sustainment strategy for H-1 Upgrade aircraft is based on three major tenets: 1) ensuring Organizational maintenance capability is optimized and that the Program Office aggressively addresses Fleet readiness issues, 2) ensuring planned Intermediate level maintenance capability is established and expanded based on approved Business Case Analysis (BCAs), and 3) ensuring organic Depot level capability, for core components, is established by focusing on components that have the greatest impact on Fleet readiness first. These three tenets are outlined in a Program Office Playbook that identifies major efforts the Program Office is implementing in support of improving Fleet readiness and sustaining the H-1 Upgrade aircraft. Detailed Plan of Action and Milestones (POA&Ms) exist for each effort and are monitored through internal Program Office reviews and other external meetings to ensure they remain on



schedule. Finally, the tenets of the H-1 Sustainment Strategy represent a combination of tactical and strategic solutions. The strategic solutions include a series of outcome based strategic solutions, supported by long-term performance based contracts to include a Captains of Industry and component Performance Based Logistics (PBL) contracts with Bell Helicopter and other key vendors. These strategic solutions are designed to improve readiness, reduce the cost per flight hour, and transition from transactional to out-come based arrangements and are foundational to the H-1 Sustainment Strategy.

### Antecedent Information

The H-1 antecedent estimate is a composite of AH-1W and UH-1N series aircraft. Cost per aircraft is the combined three-year (FY 2007 - FY 2009) average of costs reported in the Naval Visibility and Management of Operating and Support Costs Aviation Type Model Series Report database. Manpower for antecedent and upgrade aircraft are set equal as the table of organization is deemed to be equivalent. Antecedent aircraft have historically flown 21.7 flight hours per month and 260 flight hours annually. The UH-1N aircraft began retiring in FY 2010.

Annual O&S Costs BY2008 \$M			
Cost Element	H-1 Upgrades		UH-1N/AH-1W (Antecedent)
	Average Annual Cost Per Aircraft		Average Annual Cost Per Aircraft
Unit-Level Manpower	1.162		1.167
Unit Operations	0.404		0.230
Maintenance	1.448		1.510
Sustaining Support	0.096		0.110
Continuing System Improvements	0.191		0.340
Indirect Support	0.578		0.530
Other	0.000		0.000
<b>Total</b>	<b>3,879</b>		<b>3,887</b>

Item	Total O&S Cost \$M			
	H-1 Upgrades			UH-1N/AH-1W (Antecedent)
	Current Production APB Objective/Threshold	Current Estimate		
<b>Base Year</b>	33301.8	36632.0	31374.2	31597.8
<b>Then Year</b>	0.0	N/A	48822.4	N/A

### Equation to Translate Annual Cost to Total Cost

H-1 Upgrades Average Annual Cost Per Aircraft = Total O&S Cost (BY) / Total Operating Aircraft Years.

\$3.879 M Per Year Per Aircraft = \$31,374.2M / 8,089 Total Operating Aircraft Years.

O&S Cost Variance		
Category	BY 2008 \$M	Change Explanations
Prior SAR Total O&S Estimates - Dec	31776.8	

## 2017 SAR

Programmatic/Planning Factors	-129.2	Updated attrition, flight hour usage rates, and authorized aircraft allocations.
Cost Estimating Methodology	0.0	
Cost Data Update	197.6	Updated to include FY 2017 actuals.
Labor Rate	-61.9	Incorporated FY 2019 Military Composite Pay Rates and updated Contractor/Government hourly rates.
Energy Rate	77.4	Updated the fuel estimate to reflect 2020 PB rate.
Technical Input	-486.5	Updated the Flying Hour Program Reliability predictions and Depot Workload Standards for aircraft overhauls.
Other	0.0	
<b>Total Changes</b>	<b>-402.6</b>	
Current Estimate	31374.2	

<b>Disposal Estimate Details</b>
----------------------------------

<b>Date of Estimate:</b>	January 16, 2019
<b>Source of Estimate:</b>	POE
<b>Disposal/Demilitarization Total Cost (BY 2008 \$M):</b>	80.2
